

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 7/15/2022



### Recent Progress:

- Started setting structural steel joists at Department side
- Continued erection of the Apparatus Bay pre-engineered structure
- Continued interior bearing steel stud framing
- Continued exterior sheathing and green girt/insulation at Hose Tower

### Work Scheduled for Next Week:

- Finalize detail work at pre-engineered structure
- Complete hose tower masonry
- Complete steel joists and start steel decking
- Continue interior bearing steel stud framing
- Start green girt and insulation at Apparatus Bay

### Issues/Items that we are working on:

- Building Utilities: AVB awaiting design drawings from Midwest Energy for permanent power system. Received design drawings from Consumers Energy for gas service. Coordinating underground sleeving for both services.

### Project Budget and Schedule:

- Current Budget through Change Order #04: \$5,520,281  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 7.11.22

Description  
Insulated sheathing at  
Patio and soffit framing.

Taken Date  
07/15/2022 at 10:25 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3892.JPG](#)



Week of 7.11.22

Description  
Shear wall cross bracing

Taken Date  
07/15/2022 at 08:51 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3891.JPG](#)





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 7.11.22


Description  
Apparatus Bay rafters complete and strapping for insulation.

Taken Date  
07/14/2022 at 11:18 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3888.JPG](#)

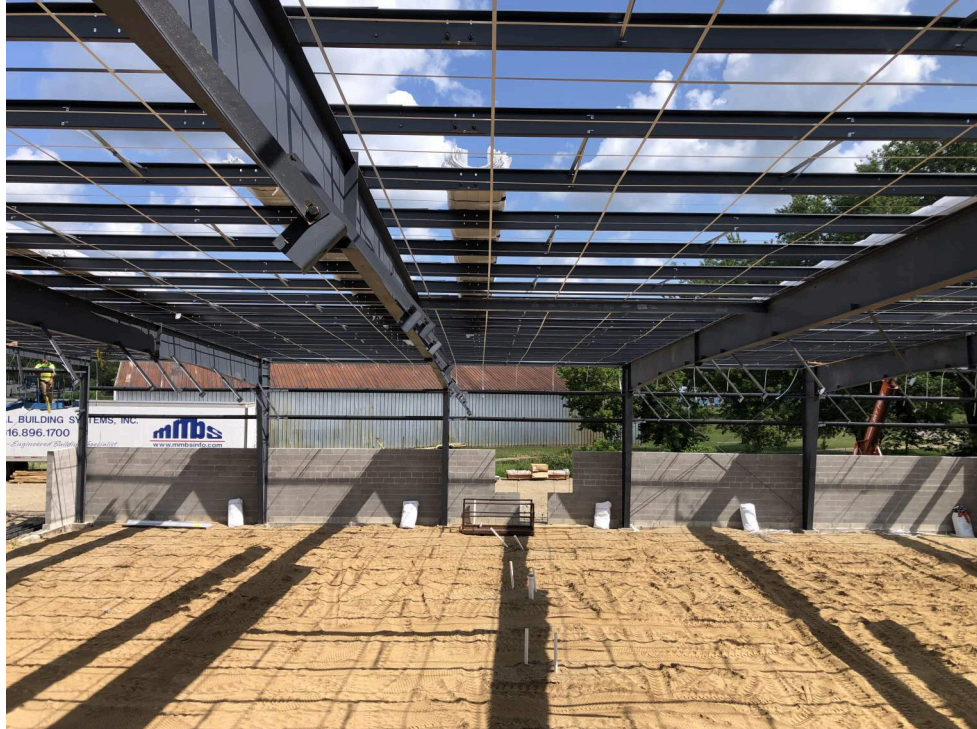

Week of 7.11.22

Description  
Green girt and insulation in hose tower.

Taken Date  
07/14/2022 at 11:14 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3884.JPG](#)





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 7.11.22

Description  
Monument sign footer.

Taken Date  
07/14/2022 at 11:12 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3883.JPG](#)



Week of 7.11.22

Description  
Insulated sheathing at  
front elevation

Taken Date  
07/13/2022 at 11:03 am

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3881.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Printed on Fri Jul 15, 2022 at 01:10 pm EDT

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 7.11.22

Description  
Steel joists in progress.

Taken Date  
07/12/2022 at 02:12 pm

Upload Date  
07/15/2022 at 12:31 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_3876.JPG](#)

