

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 7/22/2022



### Recent Progress:

- Started installation of joist bridging and steel decking at Department side
- Completed erection of the Apparatus Bay pre-engineered structure
- Completed Hose Tower masonry
- Started insulation and roof panels at Apparatus Bay
- Continued exterior sheathing at Department and green girt/insulation at Apparatus Bay
- Set hollow metal frames in masonry and steel stud bearing walls
- Completed kitchen underground plumbing rough-ins

### Work Scheduled for Next Week:

- Complete Apparatus Bay roof installation
- Continue interior bearing and non-bearing steel stud framing
- Continue green girt and insulation at Apparatus Bay
- Start apparatus bay underground rough-ins

### Issues/Items that we are working on:

- Building Utilities: AVB awaiting design drawings from Midwest Energy for permanent power system. Received design drawings from Consumers Energy for gas service. Coordinating underground sleeving for both services.

### Project Budget and Schedule:

- Current Budget through Change Order #04: \$5,520,281  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 7.18.22

Description  
Roof insulation fabric  
started over mezzanine

Taken Date  
07/21/2022 at 01:50 pm

Upload Date  
07/21/2022 at 01:53 pm

Uploaded By  
Aaron Lindsay

File Name  
[A614426A-1AEA-4A8D-8...](#)



Week of 7.18.22

Description  
Insulated sheathing and  
decking on Fire Education  
room.

Taken Date  
07/21/2022 at 01:47 pm

Upload Date  
07/21/2022 at 01:50 pm

Uploaded By  
Aaron Lindsay

File Name  
[F58E1B34-CCB2-4808-A...](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 7.18.22

Description

Steel decking installed  
over Dayroom and Kitchen  
areas

Taken Date

07/20/2022 at 03:39 pm

Upload Date


07/20/2022 at 03:40 pm

Uploaded By

Aaron Lindsay

File Name

[CFAEC3FE-04E2-42D4-A...](#)

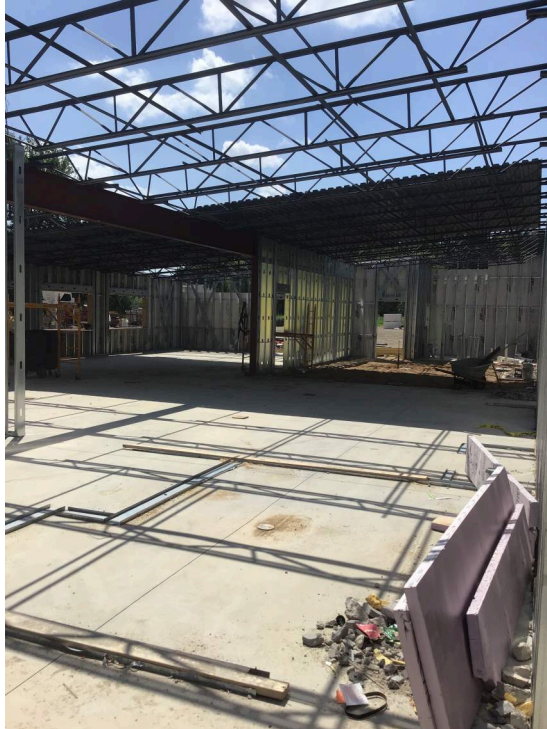

Week of 7.18.22

Description

Z-girt and iso board  
installed along north  
apparatus bay wall

Taken Date

07/20/2022 at 03:38 pm

Upload Date

07/20/2022 at 03:38 pm

Uploaded By

Aaron Lindsay

File Name

[173DC518-2841-48EC-B...](#)







BUILD SOMETHING BETTER.  
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 7.18.22

Description  
Roof insulation fabric  
installation above  
apparatus bay

Taken Date  
07/20/2022 at 03:37 pm

Upload Date  
07/20/2022 at 03:37 pm

Uploaded By  
Aaron Lindsay

File Name  
[1AC5178E-0D65-4D23-9...](#)



Week of 7.18.22

Description  
Department side roofing  
material delivered to site.  
Apparatus bay roofing  
staged on roof already.

Taken Date  
07/20/2022 at 03:36 pm

Upload Date  
07/20/2022 at 03:37 pm

Uploaded By  
Aaron Lindsay

File Name  
[6BFE6493-76A5-49B9-8...](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 7.18.22

Description  
Fabric installation over  
apparatus bay.

Taken Date  
07/19/2022 at 03:33 pm

Upload Date  
07/19/2022 at 03:33 pm

Uploaded By  
Aaron Lindsay

File Name  
[2A632651-A848-47B3-A...](#)



Week of 7.18.22

Description  
Joist bridging installation/  
welding

Taken Date  
07/19/2022 at 03:30 pm

Upload Date  
07/19/2022 at 03:30 pm

Uploaded By  
Aaron Lindsay

File Name  
[1901D888-2292-43FA-9...](#)







BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 7.18.22

Description  
Masonry wall HM window  
installation in Radio/Sec  
Storage room

Taken Date  
07/19/2022 at 03:30 pm

Upload Date  
07/19/2022 at 03:30 pm

Uploaded By  
Aaron Lindsay

File Name  
[1C1C93FA-9951-4960-8...](#)



Week of 7.18.22

Description  
HM door and window  
frame installation for Fire  
Ed. Room west wall

Taken Date  
07/19/2022 at 03:27 pm

Upload Date  
07/19/2022 at 03:28 pm

Uploaded By  
Aaron Lindsay

File Name  
[209753E1-07AD-4C85-8...](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 7.18.22

Description  
HM door and window  
frame delivered to site

Taken Date  
07/18/2022 at 03:36 pm

Upload Date  
07/18/2022 at 03:37 pm

Uploaded By  
Aaron Lindsay

File Name  
[274E24F1-E260-429D-A...](#)

