

Paw Paw Fire Station



Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 8/26/2022



Recent Progress:

- Completed interior stud framing
- Continued electrical and plumbing rough-ins in Department
- Started fire suppression piping in Apparatus Bay
- Completed precast sills at brick and started brick at Apparatus Bay 'piers'
- Continue soffit framing at Department

Work Scheduled for Next Week:

- Continue electrical and plumbing rough-ins in Department
- Continue fire suppression piping in Apparatus Bay
- Start mechanical rough-ins in Apparatus Bay and install of Mezzanine louvers
- Start fabrication of HVAC ductwork
- Continue brick at Apparatus Bay 'piers'
- Start insulation and roof panels at Department

Issues/Items that we are working on:

- Sitework to resume after Labor Day (9/6)
- Storefront Framing to start after Labor Day (9/6)
- Awaiting foundation drawings for Fire Training Structure to finalize pricing. Per Phil Butler, drawings should be complete in 2 weeks.

Project Budget and Schedule:

- Current Budget through Change Order #04: \$5,520,281
(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 8.22.22

Description
Start of brick piers at
Apparatus Bay

Taken Date
08/26/2022 at 08:28 am

Upload Date
08/26/2022 at 08:59 am

Uploaded By
Clay Stull

File Name
[IMG_4052.JPG](#)



Week of 8.22.22

Description
Start of fire suppression
piping at Apparatus Bay

Taken Date
08/25/2022 at 01:20 pm

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4049.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 8.22.22

Description
Interior stud framing
complete

Taken Date
08/25/2022 at 10:32 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4048.JPG](#)



Week of 8.22.22

Description
Fire suppression piping
fabricated and staged in
apparatus bay

Taken Date
08/25/2022 at 10:30 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4047.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 8.22.22

Description
Conference room framing
complete.

Taken Date
08/25/2022 at 07:58 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4046.JPG](#)



Week of 8.22.22


Description
Rough-ins in progress at
Day Room presentation
wall

Taken Date
08/24/2022 at 01:05 pm

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4044.JPG](#)

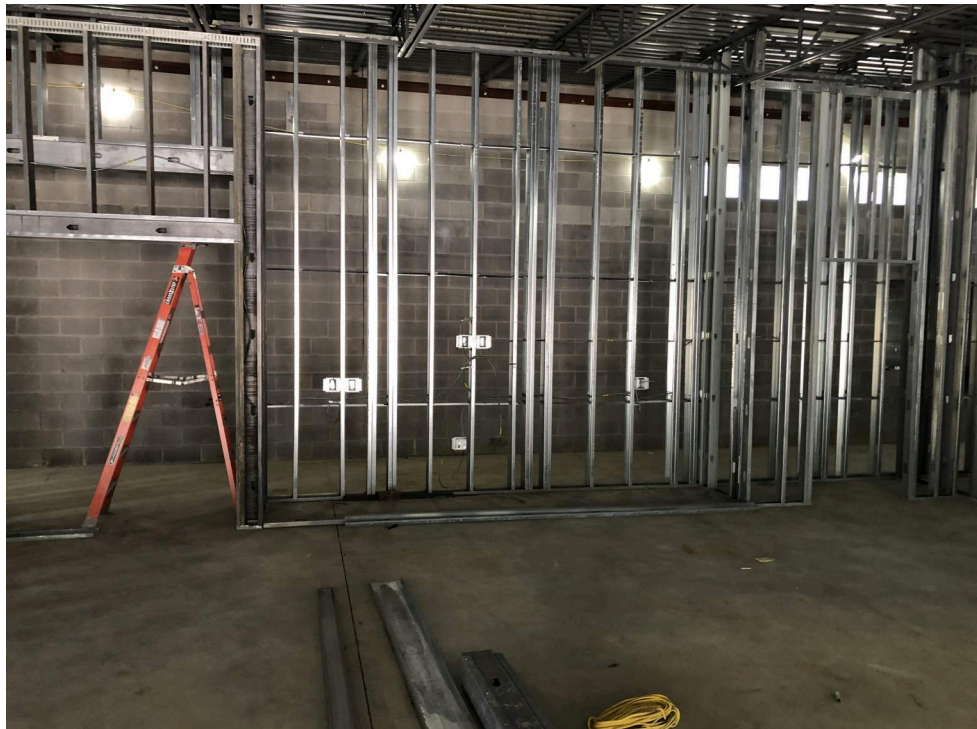



BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 8.22.22

Description
Apparatus Bay slab-on-grade complete.

Taken Date
08/24/2022 at 10:29 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4042.JPG](#)



Week of 8.22.22

Description
brick wainscoting and precast sill complete.

Taken Date
08/24/2022 at 09:53 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4041.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 8.22.22

Description
Blocking complete for
overhead door surrounds.
Will be wrapped in red
metal.

Taken Date
08/23/2022 at 10:32 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4032.JPG](#)



Week of 8.22.22

Description
brick wainscoting
complete and precast sills
in progress

Taken Date
08/23/2022 at 08:54 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4031.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 8.22.22

Description
Entry tower block in
progress.

Taken Date
08/22/2022 at 10:35 am

Upload Date
08/26/2022 at 08:58 am

Uploaded By
Clay Stull

File Name
[IMG_4024.JPG](#)

