

Paw Paw Fire Station



Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 9/16/2022



Recent Progress:

- Continue overhead rough-ins at Department including electrical, plumbing, and fire suppression
- Start hanging insulated ductwork at Department
- Continued radiant tube heater install at Apparatus Bay
- Continued Apparatus Bay overhead door install
- Continued Department roofing insulation and roofline trims
- Continued install of storefront framing windows and started glazing windows
- Installed interior hollow metal door and window frames
- Start placing concrete light pole bases
- Start re-grading storm ponds and grading gravel for site concrete and asphalt

Work Scheduled for Next Week:

- Continue mechanical rough-ins at Apparatus Bay and fabricating ductwork offsite
- Continue roof insulation and roof panel install at Department
- Continue glazing of storefront windows
- Continue overhead door install
- Start insulation and hanging drywall at Department
- Continue site grading for concrete and asphalt

Issues/Items that we are working on:

- Received engineered foundation drawings for FTS. AVB awaiting subcontractor pricing.

Project Budget and Schedule:

- Current Budget through Change Order #07: \$5,520,281
(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)
- Current Substantial Completion: November 30, 2022

Week of 9.12.22

Description
Gravel for site concrete
and asphalt

Taken Date
09/16/2022 at 09:27 am

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4159.JPG](#)



Week of 9.12.22


Description
Start of HVAC ductwork at
Department.

Taken Date
09/15/2022 at 12:56 pm

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4156.JPG](#)

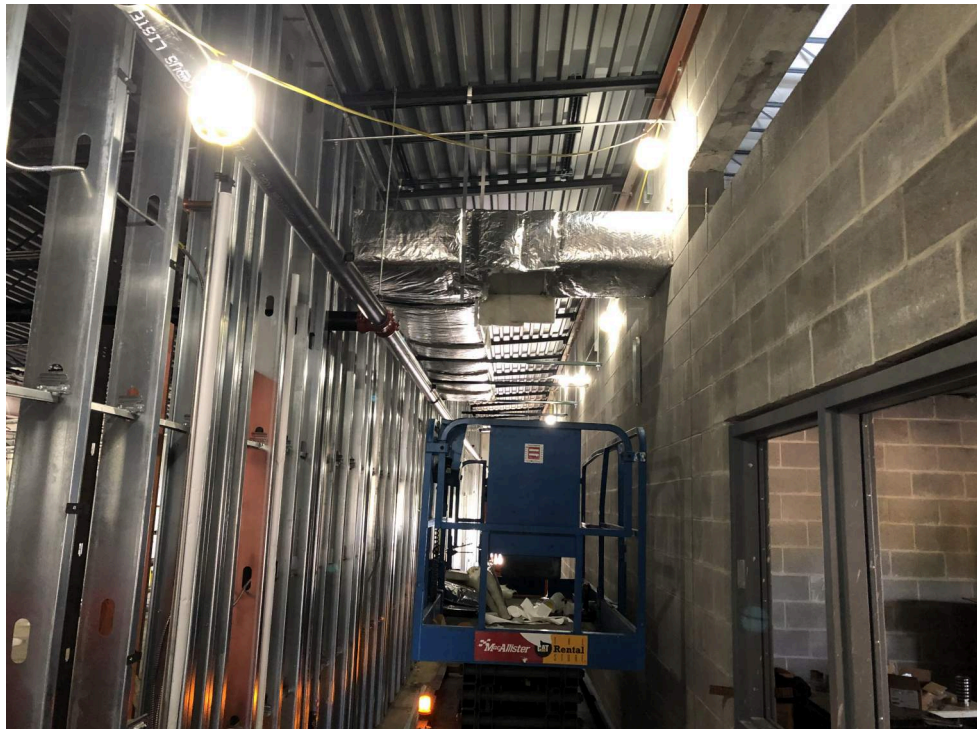



BUILD SOMETHING BETTER.
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station
832 S Gremps St
Paw Paw, Michigan 49079

Week of 9.12.22

Description

Fire Education Room storefront installed and glazed.

Taken Date

09/15/2022 at 09:10 am

Upload Date

09/16/2022 at 01:09 pm

Uploaded By

Clay Stull

File Name

[IMG_4154.JPG](#)



Week of 9.12.22

Description

Start of light pole bases.

Taken Date

09/14/2022 at 10:58 am

Upload Date

09/16/2022 at 01:09 pm

Uploaded By

Clay Stull

File Name

[IMG_4150.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 9.12.22

Description
HVAC duct staged in
Apparatus Bay

Taken Date
09/14/2022 at 08:57 am

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4147.JPG](#)



Week of 9.12.22

Description
Storefront windows
installed and glazed.

Taken Date
09/13/2022 at 01:01 pm

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4141.JPG](#)



Week of 9.12.22

Description
Brick piers on front elevation completed.
Rough grading in progress.

Taken Date
09/12/2022 at 02:39 pm

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4134.JPG](#)



Week of 9.12.22

Description
Brick piers completed on west elevation. Overhead doors in progress.

Taken Date
09/12/2022 at 11:25 am

Upload Date
09/16/2022 at 01:09 pm

Uploaded By
Clay Stull

File Name
[IMG_4130.JPG](#)

