

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 9/2/2022



---

### Recent Progress:

- Started Department roofing insulation
- Completed in wall plumbing rough-ins and passed inspection for Department
- Continued in wall electrical rough-ins in Department
- Continued fire suppression piping in Apparatus Bay
- Installed louvers at Mezzanine

### Work Scheduled for Next Week:

- Continue sitework including tie-in of sanitary and storm to building
- Continue roof insulation and roof panel install at Department
- Complete in wall electrical rough-ins and schedule inspection
- Complete fire suppression piping in Apparatus Bay and start piping in Department
- Start install of aluminum storefront framing and accept delivery of glass panels

### Issues/Items that we are working on:

- Awaiting foundation drawings for Fire Training Structure to finalize pricing. Per Phil Butler, drawings should be complete in 2 weeks.

### Project Budget and Schedule:

- Current Budget through Change Order #04: \$5,520,281  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022

Week of 8.29.22

Description  
Fire suppression piping in progress in Apparatus Bay

Taken Date  
09/01/2022 at 11:08 am

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4083.JPG](#)



Week of 8.29.22

Description  
Louvers installed at Mezzanine.

Taken Date  
09/01/2022 at 11:07 am

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4082.JPG](#)







BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 8.29.22

Description  
Apparatus Bay storm  
leads for gutters in place.

Taken Date  
09/01/2022 at 07:45 am

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4081.JPG](#)



Week of 8.29.22


Description  
Roof insulation in progress

Taken Date  
08/31/2022 at 01:58 pm

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4079.JPG](#)

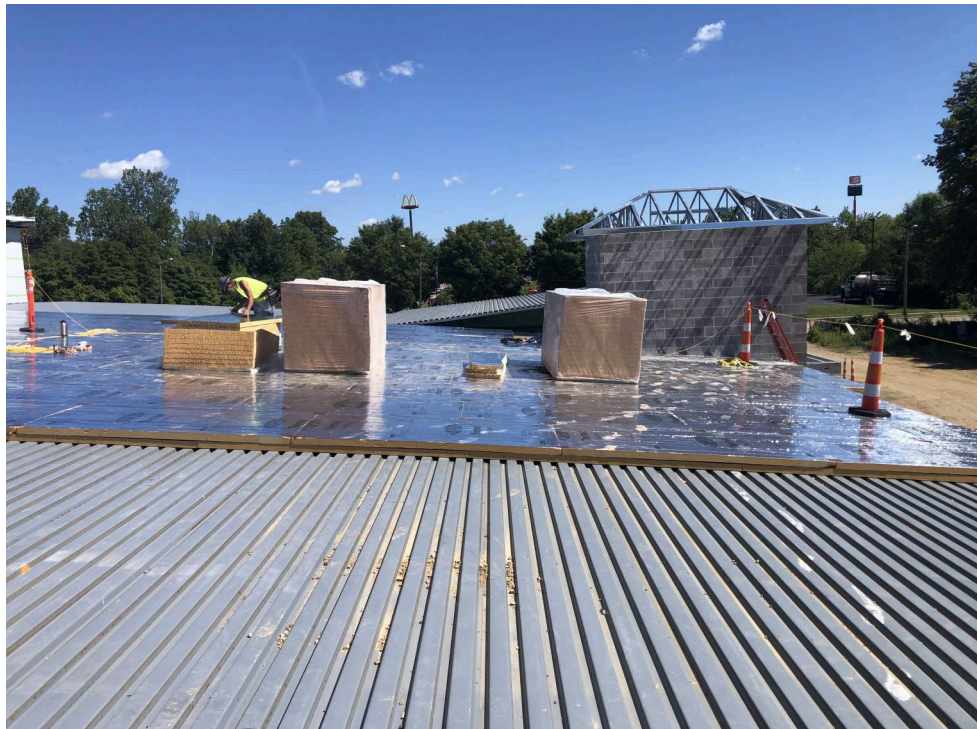



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 8.29.22

Description

Brick piers in progress at Apparatus Bay

Taken Date

08/31/2022 at 01:34 pm

Upload Date

09/02/2022 at 08:03 am

Uploaded By

Clay Stull

File Name

[IMG\\_4078.JPG](#)



Week of 8.29.22

Description

Shower sets installed as part of rough-ins.

Taken Date

08/31/2022 at 01:32 pm

Upload Date

09/02/2022 at 08:03 am

Uploaded By

Clay Stull

File Name

[IMG\\_4074.JPG](#)





Week of 8.29.22

Description  
Brick piers completed on front elevation.

Taken Date  
08/30/2022 at 09:39 am

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4066.JPG](#)



Week of 8.29.22

Description  
Plumbing rough-ins inspected and approved.

Taken Date  
08/30/2022 at 09:10 am

Upload Date  
09/02/2022 at 08:03 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4065.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 8.29.22

Description

In wall rough-ins completed. Blocking in place for casework.

Taken Date

08/29/2022 at 01:07 pm

Upload Date

09/02/2022 at 08:03 am

Uploaded By

Clay Stull

File Name

[IMG\\_4063.JPG](#)

