

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 9/30/2022



### Recent Progress:

- Continued overhead rough-ins at Department including electrical, plumbing, and fire suppression
- Continued hanging insulated ductwork at Department
- Completed Apparatus Bay overhead door install
- Continued install of Department roof panels, completed main roof and start Fire Education Room
- Set and grouted metal door frames
- Started insulation and drywall hanging in Department
- Completed re-grading storm ponds
- Continue site concrete including grading, forming, and pouring

### Work Scheduled for Next Week:

- Continue overhead rough-ins at Department
- Start layout of furnaces and MEP equipment on Mezzanine
- Continue roof panel install at Fire Education Room and start roof flashings
- Continue insulation and hanging drywall at Department
- Start drywall finishing in Department
- Continue site concrete including aprons, curbs, and sidewalks

### Issues/Items that we are working on:

- Pavilion Colored Concrete: Need color selection for 'red' concrete at Pavilion. Have color samples in trailer and will review at OAC on 10/4.
- Generator Delay: Awaiting additional information from Esper. Once received, will discuss at OAC on 10/4 and begin discussions with inspector and building official.

### Project Budget and Schedule:

- Current Budget through Change Order #07: \$5,520,281  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 9.26.22

Description

Top soil spread at south elevation. Concrete walk staked.

Taken Date

09/30/2022 at 12:33 pm

Upload Date

09/30/2022 at 01:21 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4231.JPG](#)



Week of 9.26.22

Description

East apparatus bay concrete apron poured. Glass overhead doors installed.

Taken Date

09/30/2022 at 12:32 pm

Upload Date

09/30/2022 at 01:21 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4230.JPG](#)







BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 9.26.22

Description  
Standing seam roof at  
Department in progress.

Taken Date  
09/29/2022 at 02:49 pm

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4229.JPG](#)



Week of 9.26.22


Description  
Overhead ductwork and  
sprinkler piping in  
progress in corridor.

Taken Date  
09/29/2022 at 01:00 pm

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4225.JPG](#)

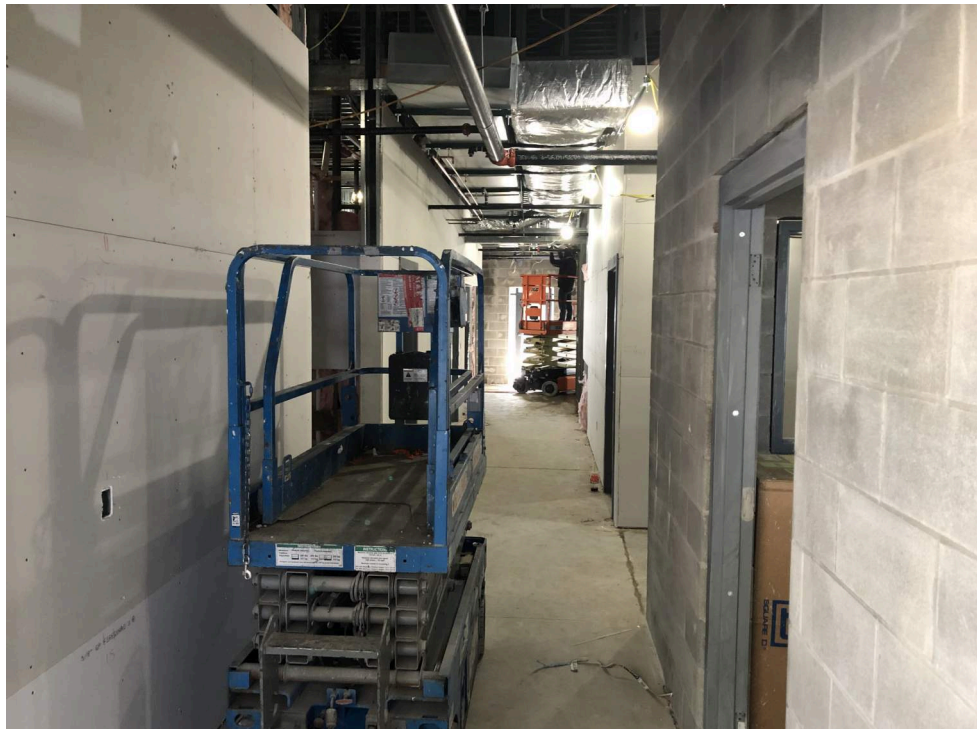





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 9.26.22

Description  
Concrete curb in progress  
at Apparatus exit drive.

Taken Date  
09/29/2022 at 10:11 am

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4223.JPG](#)



Week of 9.26.22

Description  
Drywall hanging in  
progress

Taken Date  
09/29/2022 at 09:23 am

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4222.JPG](#)







BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 9.26.22

Description  
Apparatus bay apron pour  
in progress

Taken Date  
09/29/2022 at 08:09 am

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4221.JPG](#)



Week of 9.26.22


Description  
Exterior walls insulated  
and vapor barrier install

Taken Date  
09/27/2022 at 03:10 pm

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4212.JPG](#)

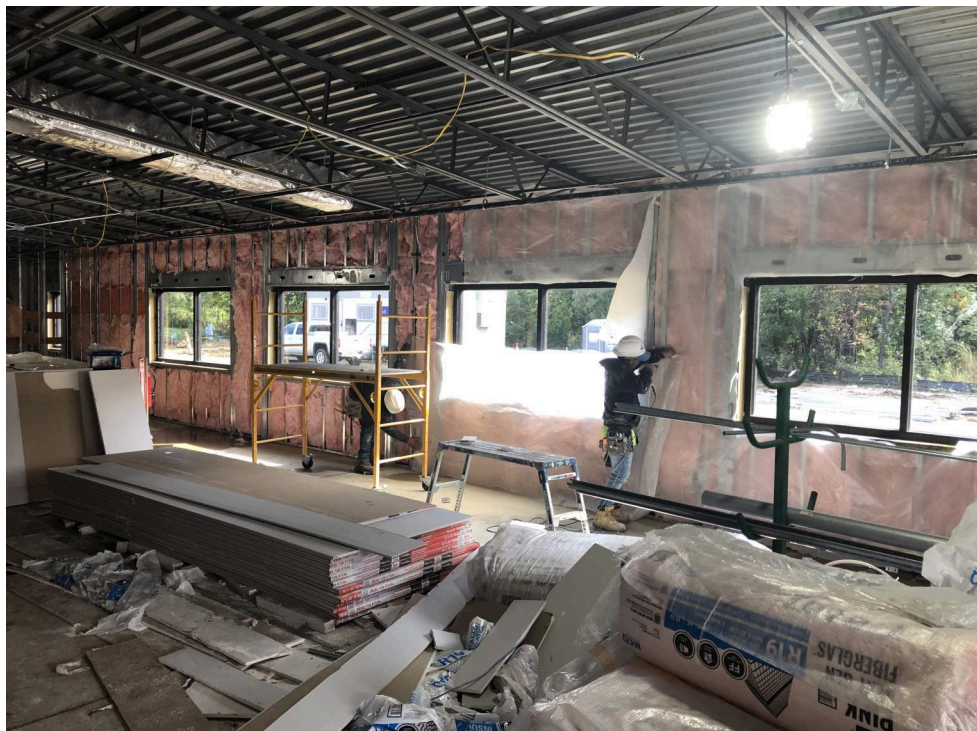





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 9.26.22

Description  
Drywall hanging in progress.

Taken Date  
09/27/2022 at 11:07 am

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4208.JPG](#)



Week of 9.26.22

Description  
Graded for sidewalk on north elevation

Taken Date  
09/26/2022 at 01:27 pm

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4205.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Printed on Fri Sep 30, 2022 at 01:47 pm EDT

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 9.26.22

Description  
drywall in progress in  
corridor.

Taken Date  
09/26/2022 at 01:05 pm

Upload Date  
09/30/2022 at 01:21 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4201.JPG](#)

