

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 10/7/2022



### Recent Progress:

- Continued overhead rough-ins at Department including electrical, plumbing, and fire suppression
- Continued hanging insulated ductwork at Department
- Set furnaces on Mezzanine
- Completed install of Department roof panels and continued work on roof trims and flashings
- Continued drywall hanging in Department
- Set temporary heater and dehumidification to allow for drywall finishing to begin
- Continue site concrete including grading, forming, and pouring
- Prepped and poured footings for future fire training structure

### Work Scheduled for Next Week:

- Continue MEP+FP rough-in and equipment install at Department and Apparatus Bay
- Continue roof trims and flashings
- Continue hanging drywall and begin finishing at Department
- Continue site concrete including aprons, curbs, and sidewalks
- Continue site grading preparing for asphalt pavement

### Issues/Items that we are working on:

- Generator Delay: Esper Electric will consult with Jim Degroff on potential battery back up light fixture solution.

### Project Budget and Schedule:

- Current Budget through Change Order #07: \$5,520,281  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022

Week of 10.3.22

Description  
fire treated plywood  
placed to allow for  
electrical panel install

Taken Date  
10/06/2022 at 10:56 am

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4267.JPG](#)



Week of 10.3.22


Description  
Ductwork and water line  
install continues in  
Department

Taken Date  
10/06/2022 at 10:55 am

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4266.JPG](#)

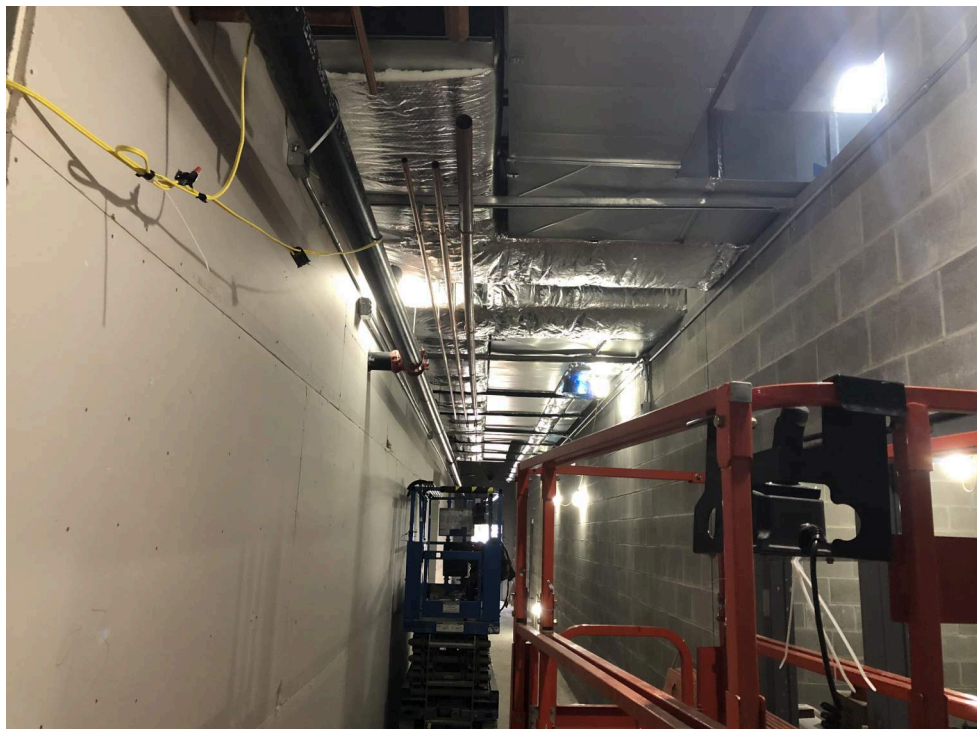



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 10.3.22

Description  
Conference room  
storefront framing in  
progress

Taken Date  
10/06/2022 at 10:55 am

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4265.JPG](#)



Week of 10.3.22

Description  
Fire suppression install  
continues in Fire Education  
Room. Insulation and  
Drywall in progress as  
well.

Taken Date  
10/06/2022 at 10:54 am

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4264.JPG](#)



Week of 10.3.22

Description  
Concrete curbing in progress on south elevation.

Taken Date  
10/06/2022 at 10:54 am

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4263.JPG](#)



Week of 10.3.22

Description  
Footings poured and piers in progress for future fire training structure.

Taken Date  
10/05/2022 at 02:40 pm

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4260.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 10.3.22

Description

Roof flashings in progress  
on Department roof

Taken Date

10/05/2022 at 09:49 am

Upload Date


10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4257.JPG](#)

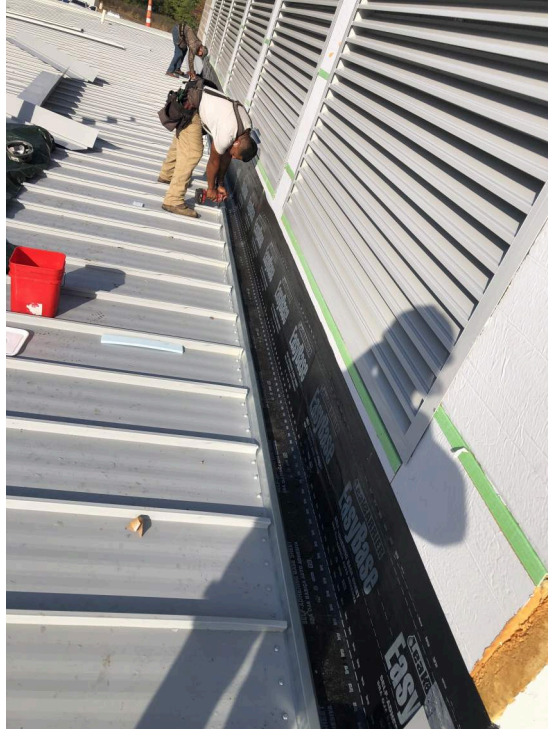

Week of 10.3.22

Description

Public sidewalks poured  
and top soil grading in  
progress

Taken Date

10/05/2022 at 08:32 am

Upload Date

10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4253.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 10.3.22

Description

Street curbing and public sidewalk placed.

Taken Date

10/05/2022 at 08:31 am

Upload Date

10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4251.JPG](#)



Week of 10.3.22

Description

Entry sidewalk formed and ready to be poured

Taken Date

10/05/2022 at 08:30 am

Upload Date

10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4249.JPG](#)





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 10.3.22

Description

Furnaces placed on mezzanine. Masonry block-filled ready for paint

Taken Date

10/04/2022 at 09:54 am

Upload Date

10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4241.JPG](#)



Week of 10.3.22

Description

West apparatus bay apron poured.

Taken Date

10/03/2022 at 03:41 pm

Upload Date

10/07/2022 at 01:15 pm

Uploaded By

Clay Stull

File Name

[IMG\\_4238.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 10.3.22

Description  
Sidewalk on north  
elevation in progres.

Taken Date  
10/03/2022 at 02:05 pm

Upload Date  
10/07/2022 at 01:15 pm

Uploaded By  
Clay Stull

File Name  
[IMG\\_4236.JPG](#)

