

# Paw Paw Fire Station



## Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 10/14/2022



### Recent Progress:

- Continued overhead rough-ins at Department including electrical, plumbing, and fire suppression
- Continued hanging insulated ductwork at Department
- Completed install of Department roof panels and continued work on roof trims and flashings
- Started install of metal panel siding trims
- Completed drywall hanging and started finishing in Department
- Continue site concrete including grading, forming, and pouring
- Set flag poles at pavilion
- Continued parking lot grading in preparation of asphalt paving

### Work Scheduled for Next Week:

- Continue MEP+FP rough-in and equipment install at Department and Apparatus Bay
- Continue installing and prepping electrical equipment for permanent power install
- Continue roof trims and flashings and roof panels at Entry Tower and Hose Tower
- Continue drywall finishing at Department
- Start block fill painting at masonry walls
- Continue site concrete including pavilion decorative concrete
- Continue site grading preparing for asphalt pavement

### Issues/Items that we are working on:

- Generator Delay: Esper Electric will consult with Jim Degroff on potential battery back up light fixture solution.

### Project Budget and Schedule:

- Current Budget through Change Order #09: \$5,550,139  
*(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)*
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 10.10.22

Description  
Start of siding trim at  
Department

Taken Date  
10/14/2022 at 11:39 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4301.JPG](#)



Week of 10.10.22

Description  
Flagpoles set at Pavilion

Taken Date  
10/14/2022 at 11:34 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4300.JPG](#)





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Week of 10.10.22

Description  
Grading for asphalt  
pavement

Taken Date  
10/14/2022 at 09:18 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4299.JPG](#)



Week of 10.10.22


Description  
Truck fill line piped.

Taken Date  
10/13/2022 at 11:32 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4297.JPG](#)

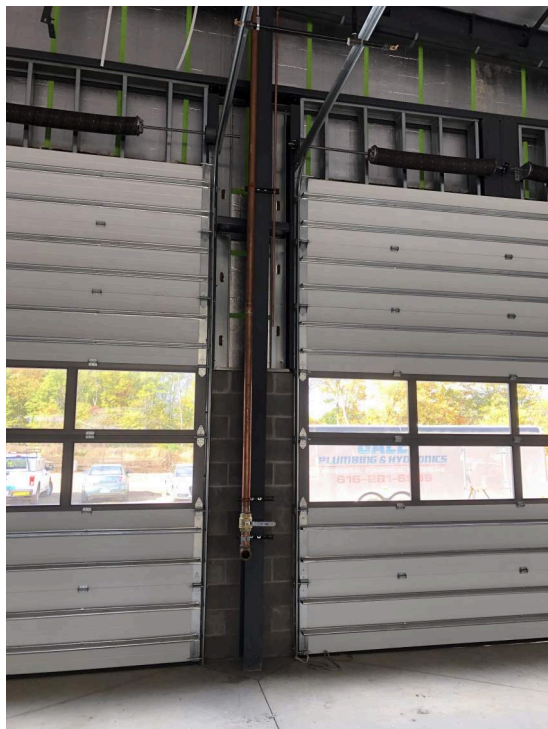



BUILD SOMETHING BETTER.  
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 10.10.22

Description  
Gravel graded for asphalt  
pavement

Taken Date  
10/13/2022 at 08:45 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4296.JPG](#)



Week of 10.10.22

Description  
Drywall finish in progress

Taken Date  
10/13/2022 at 07:35 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4294.JPG](#)



Week of 10.10.22

Description  
Drywall finish in progress

Taken Date  
10/13/2022 at 07:35 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4292.JPG](#)



Week of 10.10.22

Description  
Top soil spread around  
department

Taken Date  
10/11/2022 at 01:24 pm

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4287.JPG](#)





BUILD SOMETHING BETTER.  
AVB Construction, LLC

Job #: AVB 21-014 Paw Paw Fire Station  
832 S Gremps St  
Paw Paw, Michigan 49079

Week of 10.10.22

Description  
Kitchen Hood installed

Taken Date  
10/11/2022 at 11:34 am

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4286.JPG](#)



Week of 10.10.22

Description  
Fire Training Structure  
piers completed

Taken Date  
10/10/2022 at 01:41 pm

Upload Date  
10/14/2022 at 11:50 am

Uploaded By  
Clay Stull

File Name  
[IMG\\_4282.JPG](#)

