

Paw Paw Fire Station



Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 10/28/2022



Recent Progress:

- Continued overhead rough-ins at Department including electrical, plumbing, and HVAC
- Installed Big Ass Fan in Apparatus Bay
- Continued work on soffits and roof trims and flashings
- Continued install of metal panel siding trims and started siding panels
- Continued install of overhead door surround metal trims
- Completed drywall finishing in Department
- Continued block fill and 1st coat paint on masonry walls
- Started painting PEMB structure in Apparatus Bay
- Completed site concrete
- Completed asphalt pavement

Work Scheduled for Next Week:

- Continue MEP+FP rough-in and equipment install at Department and Apparatus Bay
- Continue installing and prepping electrical equipment for permanent power install
- Continue roof trims and flashings and roof panels at Entry Tower and Hose Tower
- Continue siding trims, flashings, and panel install
- Start priming and 1st coat paint on drywall surfaces and continue masonry block fill

Issues/Items that we are working on:

- Generator Delay: PPFd evaluating member generators for possible use otherwise will proceed with rental through Esper Electric.

Project Budget and Schedule:

- Current Budget through Change Order #10: \$5,550,139
(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)
- Current Substantial Completion: November 30, 2022

Week of 10.24.22

Description
Install of Metal Siding at
South Elevation of
Department

Taken Date
10/28/2022 at 09:25 am

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4380.JPG](#)



Week of 10.24.22

Description
Priming of Walls at
Apparatus Bay Hall

Taken Date
10/28/2022 at 09:22 am

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4379.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 10.24.22

Description
Install of Grease Duct at
Kitchen

Taken Date
10/27/2022 at 02:41 pm

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4376.JPG](#)



Week of 10.24.22


Description
Running of Water &
Sanitary Lines at
Decontamination Room
Ceiling

Taken Date
10/27/2022 at 02:41 pm

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4375.JPG](#)

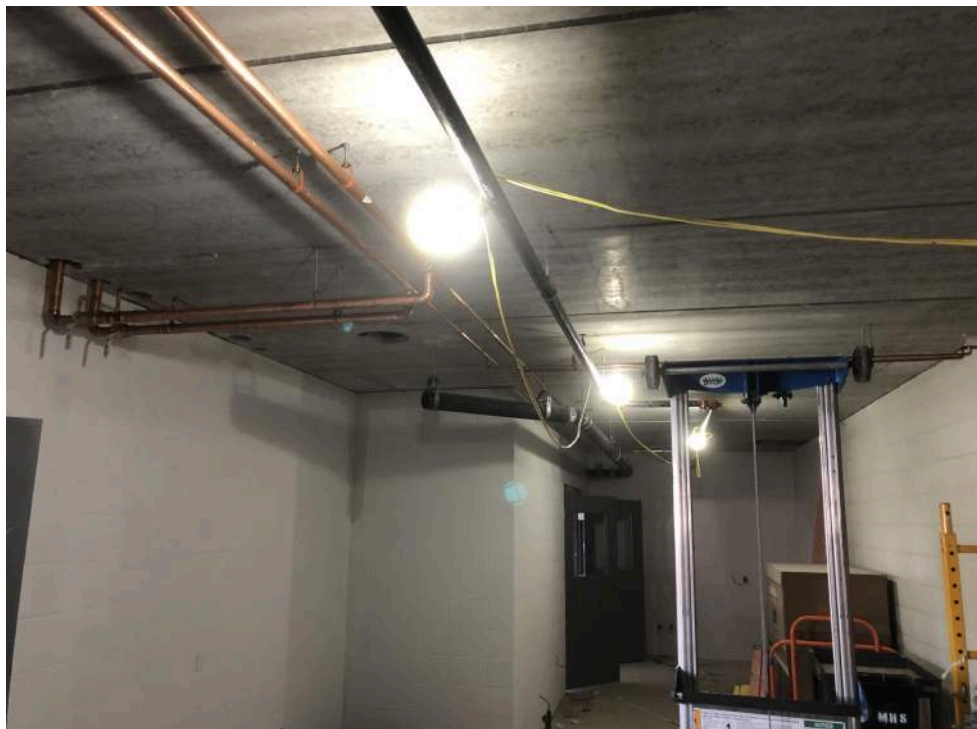



BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 10.24.22

Description
Install of Stair at Hose
Tower

Taken Date
10/25/2022 at 03:26 pm

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4364.JPG](#)



Week of 10.24.22

Description
Asphalt Paving at Back
Parking Lot

Taken Date
10/25/2022 at 02:09 pm

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4361.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 10.24.22

Description
Install of Big Ass Fan at
Apparatus Bay

Taken Date
10/24/2022 at 09:37 am

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4349.JPG](#)



Week of 10.24.22

Description
Painting of Apparatus Bay
Steel Framing

Taken Date
10/24/2022 at 09:36 am

Upload Date
10/28/2022 at 11:53 am

Uploaded By
Clay Stull

File Name
[IMG_4348.JPG](#)

