

Paw Paw Fire Station



Construction Update

832 S Gremps St, Paw Paw, MI 49079

Report By: Daniel Burns

Date: 11/11/2022



Recent Progress:

- Started low voltage installation including rack mounts, cable tray, and cabling
- Continue electrical conduit piping in Apparatus Bay and pulling wire in Department
- Continue install and set up of MDP and Panel gear. Service Transformer set
- Continue Mechanical ducting in Apparatus Bay and Mezzanine level
- Continued install of metal panel siding
- Completed primer and 1st coat paint in Department and start of Door and Frame painting
- Started tile flooring installation
- Started installation of ceiling grid
- Started installation of casework
- Started installation of landscape irrigation

Work Scheduled for Next Week:

- Continue low voltage and electrical work including cabling, wiring, and gear buildout
- Continue HVAC ducting and equipment install including kitchen ducting and Apparatus Bay
- Continue metal panel siding, fascia, soffit, and remaining roof panels.
- Continue ceiling grid and perimeter cut pads to allow for start of ceiling equipment install
- Continue tile flooring installation
- Continue installation of casework
- Start landscaping planting installation

Issues/Items that we are working on:

- Generator Delay: PPFd evaluating member generators for possible use otherwise will proceed with rental through Esper Electric.
- Penthouse Exhaust: AVB shared recent feedback from Schley Nelson to Quality Air for revised pricing. Will review with team at Tuesday's OAC meeting.

Project Budget and Schedule:

- Current Budget through Change Order #10: \$5,550,139
(This amount does not include approved changes which have not had a change order issued or Bulletins and other changes or which final pricing has not been approved.)
- Current Substantial Completion: November 30, 2022



BUILD SOMETHING BETTER.
AVB Construction, LLC

Printed on Fri Nov 11, 2022 at 02:01 pm EST

Job #: AVB 21-014 Paw Paw Fire Station
832 S Gremps St
Paw Paw, Michigan 49079

Week of 11.7.22

Description

1st coat paint in Workout room

Taken Date

11/11/2022 at 10:36 am

Upload Date

11/11/2022 at 12:53 pm

Uploaded By

Clay Stull

File Name

[IMG_4463.JPG](#)



Week of 11.7.22

Description

Mosaic floor tile in restroom. Grouting in progress

Taken Date

11/11/2022 at 10:36 am

Upload Date

11/11/2022 at 12:53 pm

Uploaded By

Clay Stull

File Name

[IMG_4462.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 11.7.22

Description
Countertop installed in
Assistant Chiefs' office

Taken Date
11/11/2022 at 09:59 am

Upload Date
11/11/2022 at 12:53 pm

Uploaded By
Clay Stull

File Name
[IMG_4460.JPG](#)



Week of 11.7.22

Description
Kitchen Make Up Air
equipment and ducting

Taken Date
11/11/2022 at 09:58 am

Upload Date
11/11/2022 at 12:53 pm

Uploaded By
Clay Stull

File Name
[IMG_4459.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 11.7.22

Description
Furnace ducting and
exhausting in progress.

Taken Date
11/11/2022 at 09:57 am

Upload Date
11/11/2022 at 12:53 pm

Uploaded By
Clay Stull

File Name
[IMG_4458.JPG](#)



Week of 11.7.22


Description
Kitchen quarry tile in
progress

Taken Date
11/10/2022 at 05:18 pm

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4449.JPG](#)

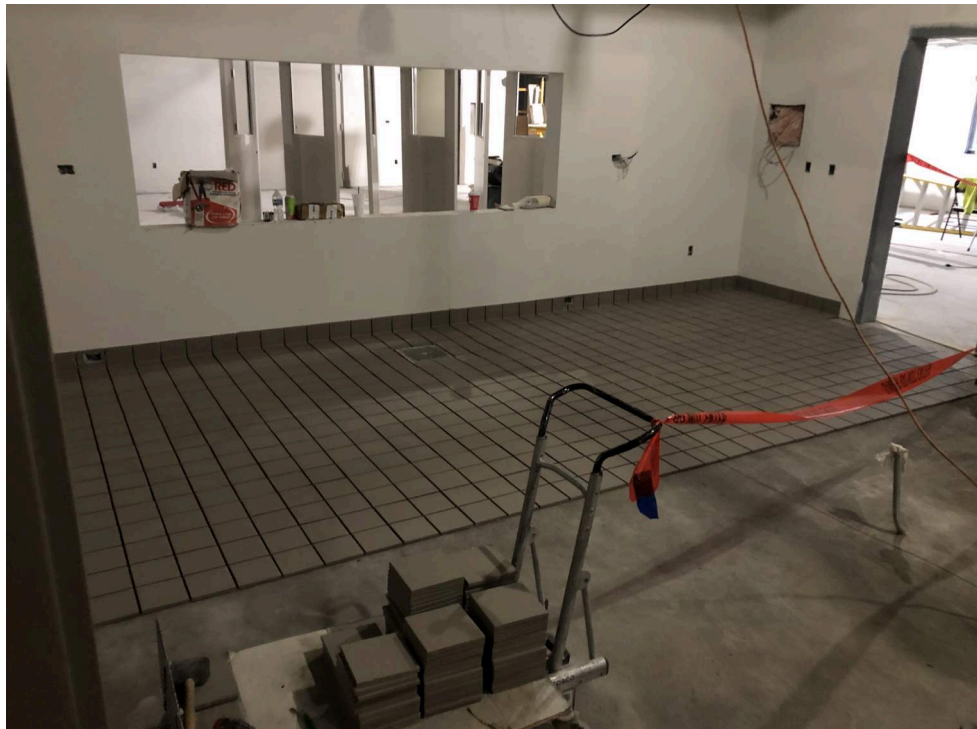



BUILD SOMETHING BETTER.

AVB Construction, LLC

Printed on Fri Nov 11, 2022 at 02:01 pm EST

Job #: AVB 21-014 Paw Paw Fire Station
832 S Gremps St
Paw Paw, Michigan 49079

Week of 11.7.22

Description

Corridor ceiling grid in progress

Taken Date

11/10/2022 at 05:16 pm

Upload Date

11/11/2022 at 12:53 pm

Uploaded By

Clay Stull

File Name

[IMG_4448.JPG](#)



Week of 11.7.22

Description

Meeting room ceiling grid in progress

Taken Date

11/10/2022 at 05:15 pm

Upload Date


11/11/2022 at 12:52 pm

Uploaded By

Clay Stull

File Name

[IMG_4445.JPG](#)

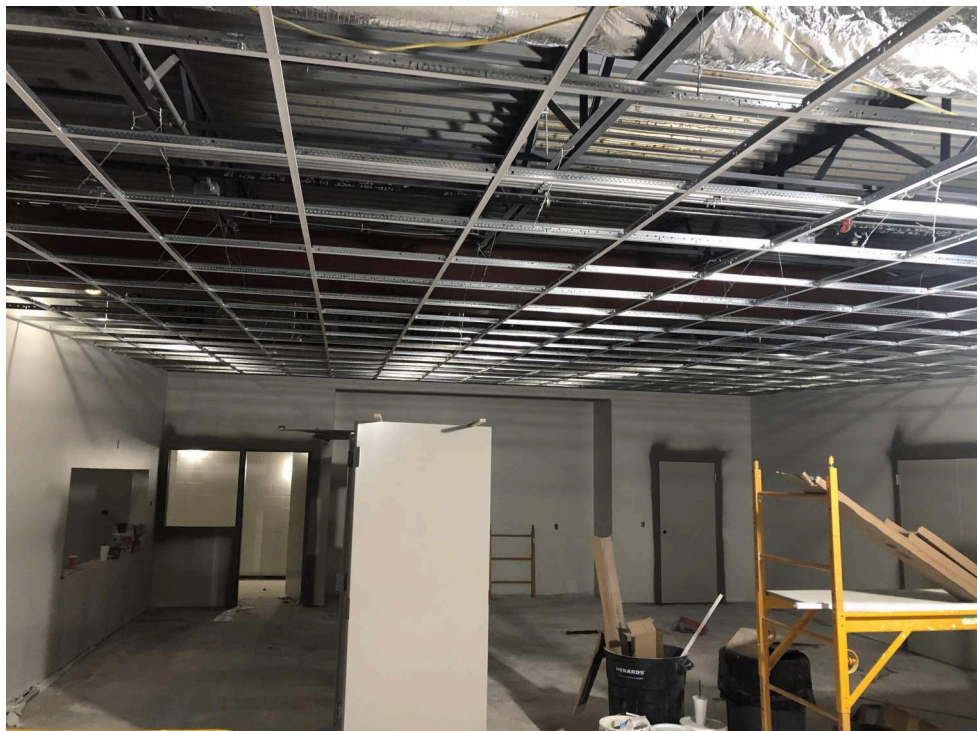



BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 11.7.22

Description
Irrigation in progress.
Pavilion concrete
complete.

Taken Date
11/10/2022 at 09:52 am

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4444.JPG](#)



Week of 11.7.22

Description
Hose tower antenna install

Taken Date
11/09/2022 at 01:40 pm

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4439.JPG](#)





BUILD SOMETHING BETTER.
AVB Construction, LLC

Week of 11.7.22

Description
Day room ceiling grid in progress.

Taken Date
11/09/2022 at 01:17 pm

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4437.JPG](#)



Week of 11.7.22

Description
Metal siding in progress on Apparatus Bay

Taken Date
11/09/2022 at 11:03 am

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4436.JPG](#)





BUILD SOMETHING BETTER.

AVB Construction, LLC

Week of 11.7.22

Description
Water service and meters
completed.

Taken Date
11/09/2022 at 10:59 am

Upload Date
11/11/2022 at 12:52 pm

Uploaded By
Clay Stull

File Name
[IMG_4434.JPG](#)

